24TH AVE S IMPROVEMENTS PROJECT

CONSTRUCTION CONTINGENCY AMENDMENT



PROJECT BACKGROUND

PUGET SOUND ENERGY (PSE) COORDINATION TIMELINE (PRE-CONSTRUCTION)




PSE COORDINATION TIMELINE (DURING CONSTRUCTION)

The City directed the contractor to resume At pre-construction meeting, construction activities. PSE transmission poles (Phase II) and Contractor notified the City about distribution poles (with communications additional conflicts with PSE gas services still attached) are in conflict Mar 2024 July 2023 Oct 2024 July 2023 June 2024 The City's project went into PSE notified the City that relocation of The City's project Suspension of Work #1. gas and distribution poles (Phase I) went into Suspension March 13th PSE relocations complete, was complete of Work #2

communications still in conflict

CONSTRUCTION COST INCREASES DUE TO PSE CONFLICTS

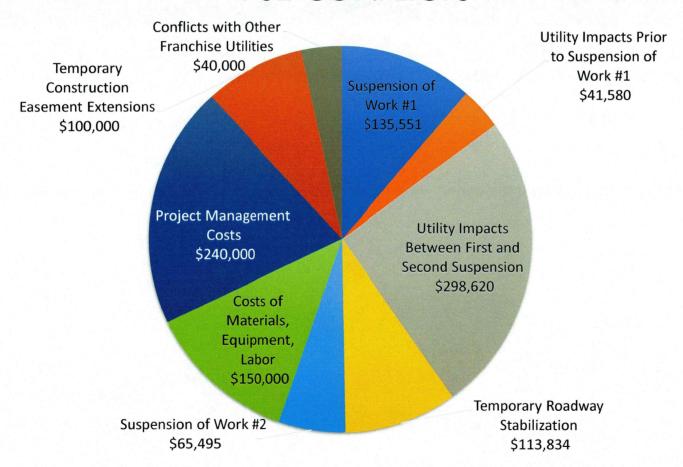

NEXT STEPS

- The 24th Ave S Improvements Project will resume construction on March 24, 2025, and the contractor expects to complete the project by October 31, 2025
- City staff met with PSE on October 24, 2024, regarding the added construction costs to the City's project and requested reimbursement of added costs due to PSE negligence
- Negotiations with PSE regarding the added construction costs related to PSE utility conflicts are ongoing

RECOMMENDED MOTION(S)

Motion I: "I move to increase the project construction contingency for the 24th Ave S Improvements Project, in the amount of \$1,185,080, bringing the total project construction contingency to \$1,887,080.

Motion 2: "I move to direct administration to bring forward a budget amendment to the 2025-2030 Capital Improvement Plan and the 2025 Capital Budget to include the amended 24th Ave S Improvements Project as described herein, and include such amendment in the next available budget amendment ordinance."
